

Adelaide University
PROJ 5001: Project Management for IT Professionals (PMITP)
DECLARATION OF CONTRIBUTION

Team No: 22473 2

The following is a declaration of your individual contributions towards this group assessment. If any contribution does not meet the assessment requirements, the course coordinator may adjust individual marks up or down, depending on the level of contribution made.

Team Member 1 Name: Sheikh Muhammad Aarib Azfar

I contributed approximately 2100 words (**excluding** the Gantt Chart) towards this assessment.

I worked on the following sections.

Section 1: Team Documents --- Team Communication Plan, Team Charter, Allocation of task agreement, Team Health Monitor and Retrospective.

Section 2: Gantt Chart --- Gantt Chart Picture

Team Member 2 Name: Shreyas Dhakal

I contributed approximately 2300 words towards this assessment.

I worked on the following sections:

Section 12: Project Closure and Knowledge Transfer

Section 13: Ethical, Cultural and Professional Considerations

Section 14: Conclusion and Recommendation

Section 15: Minutes of Meetings

Team Member 3 Name: Avishkar Waikar

I contributed approximately 1900 (excluding presentation, diagrams and charts) words towards this assessment.

I worked on the following sections:

Section 6: Scope and Requirements

(Figure 6.1 - Work Breakdown Structure (WBS),

Table 6.2 - Deliverables Table,

Table 6.3 - Functional Requirements Table,

Table 6.4 - Non-Functional Requirements Table)

Section 7: Time and Cost Management

(Table 7.1 -Project Schedule Overview,

Figure 7.2.1 - Gantt Chart Phase 1 & 2, Figure 7.2.2 - Gantt Chart Phase 3 & 4,

Figure 7.2.3 - Gantt Chart Phase 5,

Table 7.3.1 - Budget Breakdown Table,

Figure 7.3.2 - Pie Chart: Budget Allocation by category)

Final Editing of Report

Team Member 4 Name: Hariprasad K V

I contributed approximately 2760 words (including 9 tables) towards this assessment.

I worked on the following sections/questions (select whichever is appropriate).

Section 8 - Risk Management, including the risk register (Table 8.1).

Section 9 - Quality Management, including quality objectives, quality assurance processes, quality control activities and quality metrics table (Table 9.1).

Section 10 - Procurement Management, including procurement items table (Table 10.1), vendor selection criteria table (Table 10.2) and vendor management strategy.

Section 11 - Execution, Governance and Monitoring Report, including the RACI chart (Table 11.1), project communication plan (Table 11.2), KPIs and performance metrics table (Table 11.3), change request form template (Table 11.4) and project tools and software table (Table 11.5).

Team Member 5 Name: Xinxin Dong

I contributed 2036 words towards this assessment.

I worked on the following sections/questions (select whichever is appropriate).

Section 3 – Mind Map

Section 4 – Project Overview and Initiation

- 4.1 Project Background and Purpose
- 4.2 Objectives and Success Criteria
- 4.3 Business Justification
- 4.4 Project Charter
- 4.5 Stakeholder Analysis and Engagement

Section 5 – Organisational Strategy and Alignment

- 5.1 Strategic Alignment
- 5.2 Lifecycle Model and Methodology

Greenfields Organics – Supply Chain Modernisation Project

7 June 2026

Prepared by
22473 2
Sheikh Muhammad Aarib Azfar
Shreyas Dhakal
Avishkar Waikar
Xinxin Dong
Hariprasad KV |

Table of Contents

1. TEAM DOCUMENTS	4
1.1 Team Communication Plan	4
1.2 Team Charter	5
1.3 Allocation of Tasks Agreement	9
1.4 Project Team Health Monitor	11
1.5 Retrospective	18
2. GANTT CHART	19
3. MIND MAP	20
4. REPORT - Project Overview and Initiation	21
4.1 Project Background and Purpose	21
4.2 Objectives and Success Criteria	21
4.3 Business Justification	22
4.4 Project Charter	23
4.5 Stakeholder Analysis and Engagement	24
5. REPORT - Organisational Strategy and Alignment	27
5.1 Strategic Alignment	27
5.2 Lifecycle Model and Methodology	27
6. REPORT - Scope and Requirements	28
a. Project Scope Statement	29
b. In-Scope Items	29
c. Out-of-Scope Items	30
7. REPORT - Time and Cost Management	35
8. REPORT - Risk Management	39
9. REPORT - Quality Management	43
10. REPORT - Procurement Management	45
11. REPORT - Execution, Governance, and Monitoring	47
11.1 Governance and Roles	48
11.2 Communication Plan	50
11.3 Progress Tracking and Change Control	50
11.4 Tools and Software	52
12. REPORT - Project Closure and Knowledge Transfer	53

12.1 Closure Activities	53
12.2 Lessons Learned	54
12.3 Knowledge Transfer Plan	54
13. REPORT - Ethical, Cultural, and Professional Considerations.....	55
13.1 Ethics and Professional Responsibility	55
13.2 Cultural and Diversity Considerations	55
13.3 Sustainability & Social Impact.....	56
14. REPORT - Conclusion and Recommendations.....	56
14.1 Conclusion	56
14.2 Recommendations	57
15. MINUTES OF MEETINGS	57
15.1 Meeting 1	57
15.2 Meeting 2.....	59
15.3 Meeting 3	60
15.4 Meeting 4.....	61
15.5 Meeting 5.....	62
15.7 Meeting 7	63
15.8 Meeting 8.....	64
REFERENCES	66
APPENDICES	Error! Bookmark not defined.

1. TEAM DOCUMENTS

1.1 Team Communication Plan

Name	Email	Mobile	Discord	Facebook	WeChat	WhatsApp	Other
Sheikh Muhammad Aarib Azfar	sheikhmuhammadaarib.azfar@student.adelaide.edu.au	+61 438026173	aaribazfar	N/A	N/A	+61 438026173	N/A
Shreyas Dhakal	shreyas.dhakal@student.adelaide.edu.au	+61 0402109861	N/A	N/A	N/A	+61 0402109861	N/A
Xinxin Dong	Sheen.dong@student.adelaide.edu.au	0499813792	N/A	N/A	N/A	0499813792	N/A
Avishkar Waikar	avishkar.waikar@student.adelaide.edu.au	0470564358	NA	NA	NA	0470564358	NA
Hariprasad K V	hariprasad.kv@student.adelaide.edu.au	0411883536	N/A	N/A	N/A	0411883536	N/A

1.2 Team Charter

Team Purpose	
What is the purpose of the team and what are the outcomes to be achieved by the team? The purpose of this team to collaborate and work together to plan, manage and follow project management principles and methodologies. The outcomes will be to successfully deliver highest quality work which clearly showed application of project management processes, and we aim to produce work which involve getting HD grade in this course and standards throughout the assignment.	
List all team members and identify the team leader.	
1. Sheikh Muhammad Aarib Azfar (Lead) 2. Shreyas Dhakal 3. Avishkar Waikar	4. Hariprasad K V 5. Xinxin Dong
Duration and Time Commitment	
Document the amount of time the team will be working together and the estimated amount of time that will be dedicated weekly/monthly to the project. Our team is committed to work on this project until it is fully done and submitted. So we can estimate that we, individually will spend around 5 hours per week to get through task assigned and around 4 hours per week extra in final stages to work together when finalizing the report.	
Deliverables	
Define the outputs to be produced by the team. Include the documents to be produced and the deadlines for when each deliverable is due. Based on the task allocation these the outputs and documents required by each team member to complete before our deadline set. Aarib: Team Documents: Team Charter, Team Communication Plan, Allocation of Task Agreement, Project Team health Monitor, Retrospective and Gantt Chart. Deadline: 6 June 2026	

Shreyas: Project Closure and Knowledge Transfer, Ethical, Cultural, and Professional Considerations, Conclusion and Recommendations and Minutes of Meetings. Deadline: 6 June 2026 Avishkar: Scope and Requirements, Time and Cost Management, Final Editing of report, Project Presentation and editing of Project Presentation. Deadline: 6 June 2026 Hari: Risk Management, Quality Management, Procurement Management and Execution, Governance, and Monitoring. Deadline: 6 June 2026 Xinxin: Mind Map, project overview and initiation, Organisational Strategy and Alignment and Submission of Report and Presentation. Deadline: 7 June 2026	
What will you do if someone...?	
Can't make it to a meeting.	The meeting will be recorded, share it to absent member along with meeting minutes. A follow-up meeting could be held if needed.
Doesn't agree with the way things are being done.	Arrange a meeting, when one does not agree. Listen and review his concerns openly, weigh the advantages and disadvantages of the approaches being discussed. Lastly review the impact it could have on our project timeline and then finalise the decision with everyone agreeing and especially the team member who didn't agree in the first place.
Doesn't understand what to do.	The team member who did not understand must ask to clarify with the team members. It their job to be responsible and ask. Otherwise they can go through the meeting minutes, project documents and tasks, if only they believe they can proceed thought without help of another team member.
Feels they're doing more than the others.	Once again, team member must communicate and address their concerns. We as a team will look into to it and discuss accordingly. Finally, we will reassign tasks accordingly and as per discussion.
Feels everything is running behind schedule.	The team reevaluate our tasks and timeline against the deadline of the project. We will then reallocate and reprioritise task. We

	will also allocate more time, adjust deadlines and encourage collaboration for the tasks that are running behind on time.
Doesn't say much at meetings.	We must make sure that our environment is friendly and comfortable for everyone to speak. We will try to make meeting an open floor where everyone can talk and be heard. We will encourage and allocate equal time for everyone to speak.
How will you...?	
Allocate tasks.	The tasks will be allocated based on a mixture of personal preference and amount of the work to be done. We will make sure that everyone has equal contribution according to their tasks. Also, we will keep in mind about each member availability and skill level when we will be deciding to split the tasks.
Prioritise.	Tasks will be prioritised based on its difficulty, urgency, dependency. Each task will also be judged based on comments and feedback given from our team members and teachers.
Ensure everyone gets their work done.	Set deadlines for our tasks and monitoring its progress. We make an environment where everyone is in this together that we should complete our tasks. Also, we have set a consensus that we need to get this done in the highest standards.
Stay in contact with each other.	A WhatsApp group has been created for quick and easy communication. The comment feature in word will also be used in specific communication. In person meeting will also be held when necessary.
Run your meetings.	We will use Google meetings to hold quick online meeting. We will also hold meeting in person when necessary. We have made sure that meeting minutes will be recorded to highest standards as it is the requirement in the report.
Additional questions...	
How often will you meet up together?	We will meet at least once a week to ensure that we have consensus and get more information relating to the project. Additional meeting can be set up if required.

What roles should be taken on in the group?	Roles will be based on each group member skill and tasks. However, everyone will help each other and try to take initiative of tasks, this includes but not limited to work on them or to deal with the comments from the instructors.
How will everyone's progress be kept track of?	Since we have our allocation of task agreement document, we have a simple checklist for tasks. To check the progress, look at the report and go through its history/timeline. Meeting discussions will be used to ensure that we have ownership and that everyone is committed to complete this report.
What other potential problems do you think the group could have?	The most significant limitation we have is finding a common time to work together. We also could have differences in work styles, quality and methodologies on how to get it done.

1.3 Allocation of Tasks Agreement

Task	Aarib	Shreyas	Avishkar	Hariprasad	Xinxin
1.Team Documents	L, C	C	C	C	C
1.1 Team Communication Plan	L, C, E	C	C	C, E	C
1.2 Team Charter	L, C, E	C	C, E	C	C
1.3 Allocation of tasks agreement	L, C, E	C, E	C, E	C, E	C, E
1.4 Project Team Health Monitor	L, C, E	C, E	C,	C	C
1.5 Retrospective	C	C	C, E	C	L,C,E
2. Gantt Chart	L, C, E	C	C, E	C	C
3. Mind Map	C	C,	C, E	C	L, C, E
4. Report – Project Overview and Initiation	C	C	C, E	C	L, C, E
5. Report – Organisational Strategy and Alignment	C	C, E	C	C	L, C, E
6. Report – Scope and Requirements	C, E	C	L, C, E	C	C
7. Report – Time and Cost Management	C	C	L, C, E	C, E	C
8. Report – Risk Management	C, E	C	C	L, C, E	C

9. Report – Quality Management	C, E	C	C	L, C, E	C
10. Report – Procurement Management	C, E	C	C	L, C, E	C
11. Report – Execution, Governance, and Monitoring	C	C, E	C	L, C, E	C
12. Report – Project Closure and Knowledge Transfer	C	L, C, E	C	C	C, E
13. Report – Ethical, Cultural, and Professional Considerations	C	L, C, E	C, E	C	C
14. Report – Conclusion and Recommendations	C, E	L, C, E	C	C	C
15. Minutes of Meetings	C, E	L, C, E	C	C	C
16. Final Editing of Report	C	C, E	L, C, E	C	C
17. Presentation Content	C	C	C, E	L, C, E	C
18. Final Editing of Presentation	C	C, E	C, E	L, C, E	C
19. Submission of Report and Presentation	C	C	C, E	C	L, C, E

1.4 Project Team Health Monitor

Attributes	Checkpoint 1	Checkpoint 2	Checkpoint 3
Team cohesion			
Balanced team			
Encouraging difference			
Shared understanding			
Value and metrics			
Suitable ways of working			
Encouragement and support			
Continuous improvement			

Commented [SH2]: Possibly make this white please as it is currently a bit hard to see.

Attributes	Example	Checkpoint 1	Comments
Team cohesion			Justification: From the start, the team had a consensus to succeed and for that to happen, we communicated well and were respectful to everyone. Next steps: Keep continuing whatever is going on and encourage others to speak for additional input.
Balanced team			Justification: The team was balanced, everyone had what it took to get this work done. Everyone's skills were top notch. Next steps: Just ensure that work is divided equally so no one burns out and affects the team.
Encouraging difference			Justification: We shared amazing ideas however we settled for what was said, rather than thinking extra or challenging any ideas. Next steps: Try to think outside of the box to induce more in-depth ideas. Try not to be a yes man.
Shared understanding			Justification: We understood what we wanted however there were some misinformation, which was still there which hindered our progress Next steps: Try to review the documents and ask questions rather than assuming things.
Value and metrics			Justification: We had the goals in mind but lacked ant metric which could show our progress to complete the goal

Commented [S(3): @Sopheara Hean, Do we remove this example column.

Commented [3R2]: No the example column with the example ratings can stay there

			Next steps: Define clear measurable goals and track them to ensure that we complete this project.
Suitable ways of working			Justification: We just could not find a way to work that fitted everyone styles of work. Everyone had their own methods of working. Next steps: Have a folder where every document was visible to everyone and establish meeting and communication protocols.
Encouragement and support			Justification: Everyone was willing to help or take initiative but only few helped or supported. Next steps: 1. Take more initiative and support each other by checking out the report content and provide suggestions to improve 2. Ask for help if stuck at some points and be ready to help if done with one's work
Continuous improvement			Justification: Judging by the fact that we were randomly selected as a team, we had good chemistry when comparing to new teams, so it was a success Next steps: Learn about our objectives and work towards them for the success of the project and improvement for the team.

Commented [SH4]: Some of these sections could be expanded a bit further. i.e., how can you take initiative and support each other? Provide some specific and actionable steps.

Attributes	Example	Checkpoint 2	Comments
Team cohesion			Justification: We encouraged others to speak more often and collaboration among us have increased. Next steps: Maintain consistent communication and take initiative for overall progress
Balanced team			Justification: The works was divided equally, and everyone understood their tasks and were working towards them. Next steps: If your task is finished, try to help other and offer them your expertise.
Encouraging difference			Justification: We started to think deeply about the ideas and had discussions. However, we still lacked in ideas to challenge others. Next steps: Maintain constructive discussions and challenge when appropriate.
Shared understanding			Justification: We understood our roles perfectly and asked when misunderstood. However, we could not track our roles effectively Next steps: Try to not assume and track our roles
Value and metrics			Justification: We had measurable tasks which we monitored to see our progress against the project deadline. Next steps:

			Keep up the work and try to identify risks if any.
Suitable ways of working			Justification: Again, we just could not find a way to work that fitted everyone styles of work. From our teacher's point of view, our work was still pending even though we were confident. Next steps: Speed up our work and try to maintain efficiency.
Encouragement and support			Justification: We started taking initiative more regularly. However, we still lacked support from our team. Next steps: Try to maintain support and promote open teamwork.
Continuous improvement			Justification: We successfully understood our objectives. We learned from our mistakes and showed improvement. Next steps: Try to reflect on our work to make it even better. Question ourselves and our ways of working to improve together as a team and individuals.

Attributes	Example	Checkpoint 3	Comments
Team cohesion			Justification: We contributed more often; This was our best work comparatively. We started to trust others. Next steps: Keep up the enthusiasm and energy habits undertaken from this project.
Balanced team			Justification: We did the best work, showing out teams' skill and hard work. We delivered the project successfully. Next steps: Try to keep in contact with team for future work.
Encouraging difference			Justification: We still had constructive discussions. We tried to challenge ideas which brought even better ideas. We just did not fully challenged others. Next steps: We should learn from this and apply these habits in future team projects.
Shared understanding			Justification: We completely understood what the deliverables were and delivered the best project. Next steps: Keep up the good working ways, consistent communication and understanding.
Value and metrics			Justification: Our project was tracked perfectly, we did not miss the deadline, we were well done before our deadline. Next steps:


			Learn from these metrics and apply in future team situations.
Suitable ways of working			Justification: We finally worked together, got ourselves together for the best work. However, it was a bit late in the project. Next steps: Learn from the mistakes and apply these as soon as other project starts.
Encouragement and support			Justification: The team consistently supported and encouraged others to do their best work. We had a positive environment where everyone was comfortable. Next steps: Try to be consistent and apply these in future project.
Continuous improvement			Justification: Due to our improvement throughout the project, we hit a flow state in final stages of our project. We learned from our mistakes and reflections. Next steps: Try to learn from our mistakes in future projects

1.5 Retrospective

WHAT WENT WELL?	WHAT COULD HAVE GONE BETTER?
○ We had strong communication through our WhatsApp group, which enabled us to complete our work effectively. ○ The tasks were divided fairly based on its difficulty and length. ○ We supported and helped other when questions arose. ○ We created a comfortable environment, where everyone was encouraged to speak and share ideas.	○ We could not find the best time to work together. ○ Some of our task were taking longer than expected which somewhat delayed us ○ We did not really challenge ideas in order to produce top quality ideas.
WHAT WILL WE TRY NEXT?	WHAT QUESTIONS DO WE HAVE?
○ Try to Track our project much more in depth and define measurable milestones. ○ Learn from our mistakes and do self reflections to keep improving our self. ○ Try to find a common time and conduct regular formal meetings.	○ How do we find an common time when everyone has their own time where they work in? ○ How do we try to enforce or encourage a same style of work, when everyone has their own style or methodology of working? ○ Is setting an internal deadline a few earlier than official deadline helpful in our specific team environment?

Commented [SH5]: Section 1 should be filled out. Apart from the retrospective and health monitor 2 and 3. Needs to be done ASAP.


2. GANTT CHART

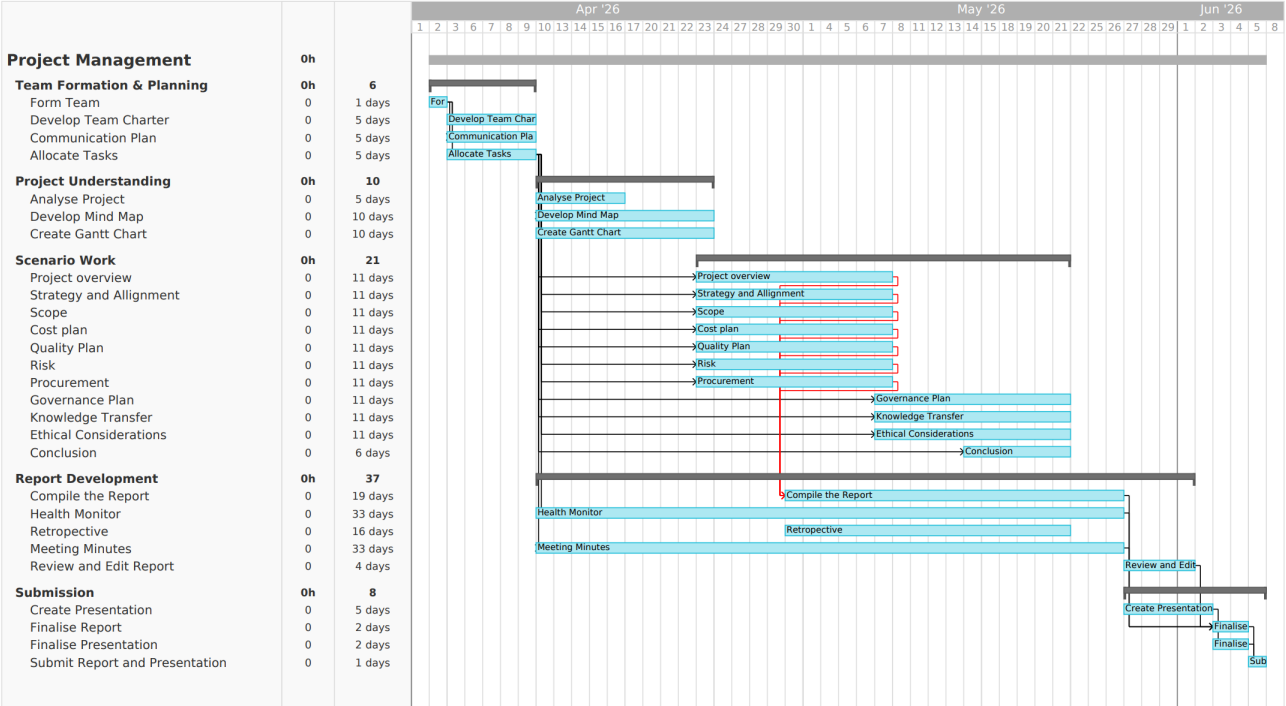

Commented [SH6]: Where is this?

Commented [MS6R2]: Missing Gantt Chart of your assignment represents a plan of how you will complete this assignment. Should provide for now the hyperlink to Gantt Chart and then later the image of the Gantt Chart.

3. MIND MAP

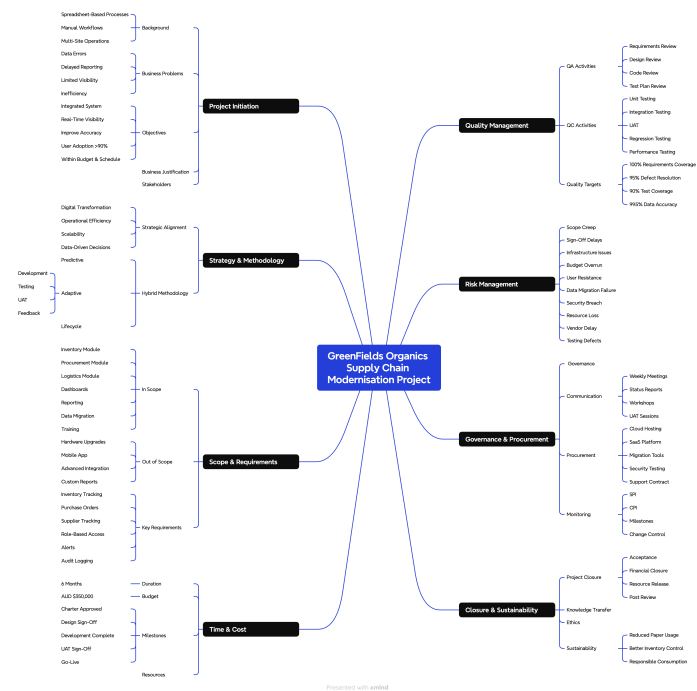

Commented [SH7]: Mind map is good but a bit more detail could be provided. I.e. specifically mention what is in scope and what is out of scope?

4. REPORT - Project Overview and Initiation

4.1 Project Background and Purpose

GreenFields Organics operates as a regional agribusiness with supply chain activities distributed across multiple locations. At present, the organisation relies heavily on spreadsheet-based systems and manual workflows to manage key operations such as inventory control, procurement processes, and logistics coordination. These processes handle inventory tracking, procurement, and logistics coordination involving multiple sites. While this approach may have been sufficient at similar and smaller scale. It has the potential to become inefficient since the organisation growing.

The current system presents several operational challenges. The reliance on manual data entry and disconnected systems has led to several operational challenges such as time-consuming processes, high risks of human errors and poor integration between functions. Furthermore, the lack of real-time data visibility may limit the management's ability to monitor stock levels, track procurement activities, and respond quickly to operational issues. As a result, the organization may experience inefficiencies, delays, and difficulties in maintaining optimal operating.

From the business perspective, these challenges effectively affect operational performance and consume unnecessary time and resources, while inaccurate and delays slow down the efficiency. These problems create a requirement for a more integrated and reliable system which can support this organization optimally running.

The purpose of this project is to develop and implement an integrated IT system that give a solution to moderate GreenFields' supply chain management processes. The system will aim to improve and solve data accuracy and real-time reporting and coordination between inventory procurement, and logistics functions. Ultimately, the project focuses on enhancing operational efficiency, reduce errors, and provide a scalable foundation for future growth.

4.2 Objectives and Success Criteria

The objective of this project is to deliver a modernised and integrated supply chain management solution that can enhance and support enterprise operational efficiency, data management and decision-making capabilities within GreenFields Organics.

The project is guided by the following objectives:

1. To design and implement an integrated system which can cover and consolidates the core functions such as inventory, procurement, and logistics into a unified IT platform within a six-month timeframe.
2. To improve data accuracy and management by reducing reliance on manual processes and minimising human errors in supply chain operations.
3. To provide real-time data visibility to support operational monitoring and strategic decision-making.
4. To enhance process efficiency by streamlining workflows and reducing delays associated with manual reporting.
5. To ensure effective system adoption through structured training programs and user support materials.

Project success will be assessed against the following measurable criteria:

1. Completion of system deployment within the defined schedule and budget constraints.
2. Demonstrated the reduction in manual processing flows and operational inefficiencies.
3. Availability of real-time dashboards and reports to key stakeholders.
4. Achieving a minimum of 90% user adoption rate following system implementation.
5. Positive stakeholder feedback regarding system usability and performance.

4.3 Business Justification

GreenFields Organics is currently facing operational inefficiencies due to the reliance on manual workflows and spreadsheet-based system for managing chain activities. These limitations result in several problems which slow the processes down. As the organization continues to grow these issues are expected to be addressed, otherwise those problems may become more significant.

To address these challenges, this project proposes the implementation of a modern integrated supply chain management system. This justification for this project can be evaluated in terms of operational, financial and strategic benefits.

From operational aspect, this system will significantly improve efficiency by reducing manual tasks and minimising errors. Automated inventory tracking and procurement processes will allow staff to

perform their tasks more quickly and accurately. Moreover, data visibility will also improve coordination between departments.

From financial aspect, the project is expected to reduce costs what associated with inefficiency such as overstocking, stork shortages and reworking by data issues. Improved procurement tracking will also enhance budget control and reduce unnecessary expenses.

From strategic aspect, the implementation of a modern IT system supports long-term growth and digital transformation. This system will provide a scalable platform which can accommodate future expansion and evolving requirements. Additionally, improved data visibility will enable better strategic planning and informed decision making.

Overall, the proposed project is justified by ability to solve current operational challenges while delivering measurable business benefits and supporting long-termly.

4.4 Project Charter

Project Title

GreenFields Organics Supply Chain Modernisation Project

Project Purpose

This project is aiming to modernise GreenFields Organics' supply chain operations through the implementation of integrating an IT solution to instead the traditional paper operating, this can enable to improve efficiency, enhanced data visibility and supporting making effective decision by managements.

Objectives

This project seeks to deliver a scalable and integrated IT system within limited period and budget constraints, while improving operational efficiency, reducing human errors, and supporting user adoption through training and documentation.

Scope Overview

This project will include the design and implementation of a supply chain IT system which covering inventory, procurement, and logistics functions. It will also include reporting capabilities and user training. Activities such as hardware procurement, mobile application development, and advanced third-party integrations are excluded from this project scope.

Stakeholders

Key stakeholders include executive sponsors, operational managers, finance personnel, warehouse staff and the project delivery team.

Schedule and Budget

The project is planned for completion within six months, with an allocated budget of AUD \$350,000.

Risks and Assumptions

The project faces potential challenges, including user resistance, integration issues, and the possibility of cost overruns. The model is based on the assumption that there will be stakeholder engagement, that resources will be available, and that there will be adequate technical infrastructure.

Project Governance Authority

The Project Manager is responsible for overseeing project execution, managing resources, and ensuring alignment with project objectives. Decisions of a major nature and escalations will be directed to the project sponsor.

4.5 Stakeholder Analysis and Engagement

1. Stakeholder Identification

Stakeholders are individuals or groups who can influence or are affected by the project. In this project, key stakeholders include both internal and external parties involved in or impacted by the supply chain modernisation initiative.

The primary stakeholders are:

- GreenFields CEO (Project Sponsor)
- Operations Manager

- Finance Manager
- Warehouse Supervisor and operational staff
- TechNova Project Manager and project team
- External vendors or service providers

These stakeholders have varying levels of influence, interest, and expectations, which must be carefully managed to ensure project success.

Stakeholder Analysis

To effectively prioritise stakeholder engagement, a Power-Interest analysis is applied. This analysis method can be used to categorise stakeholders as well as determine appropriate engagement strategies. (Mints & Evelina, 2019).

Commented [SH8]: Could consider placing this in a table format.

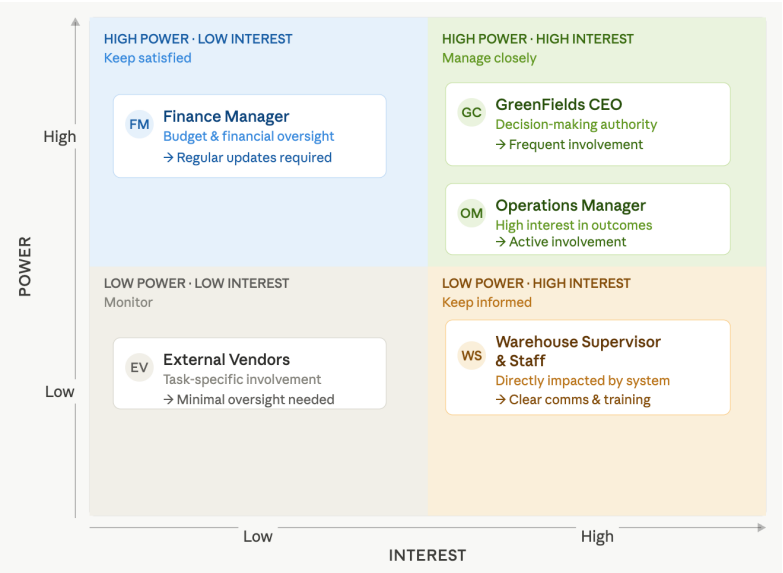


Figure 4.5 - Power-Interest analysis

This structured analysis ensures that engagement efforts are prioritised based on stakeholder influence and interest levels.

Stakeholder Engagement Strategy

Effective stakeholder engagement is essential to ensure alignment, reduce resistance, and support project success. Engagement strategies are tailored based on stakeholder needs and levels of influence.

CEO (Project Sponsor): Engage through regular executive briefings and milestone reports to ensure alignment with strategic goals and secure ongoing support.

Operations Manager:

Collaborate closely through workshops and review sessions to ensure system requirements align with operational needs.

Finance Manager:

Provide periodic financial updates and reports to maintain transparency and support budget oversight.

Warehouse Staff:

Engage through training sessions, user demonstrations, and feedback mechanisms to ensure usability and encourage adoption.

Project Team:

Maintain continuous communication through meetings, collaboration tools, and progress tracking systems.

Internal project stakeholders also include the Business Analyst, Developers, QA/Test Lead, and Training Coordinator from TechNova Solutions.

External Vendors:

Manage through formal agreements, progress monitoring, and regular coordination meetings.

By applying structured engagement strategies, the project aims to ensure stakeholder alignment, minimise resistance, and facilitate successful system implementation.

5. REPORT - Organisational Strategy and Alignment

5.1 Strategic Alignment

Projects deliver the greatest value when they are aligned with broader organisational strategy rather than operating in isolation. Strategic alignment ensures the project outcomes which contribute directly to organisation's goals and long-term values. (Kerzner, 2022) In the case of GreenFields Organics, the proposed supply chain modernisation initiative supports several key strategic priorities, including operational efficiency, digital transformation, and data-driven decision-making.

The current reliance on manual workflows limits the scalability and reduces organizational agility. By implementing an integrated IT-based solution, the project enables GreenFields to modernise critical operational processes and improve coordination across inventory levels, procurement, and logistics functions.

Strategically, the project enhances the organisation's ability to manage growth, improve responsiveness, and maintain operational visibility across multiple locations. The availability of real-time information also strengthens managerial decision-making and supports future innovation initiatives.

Furthermore, the project establishes a scalable technological foundation of supporting future business expansion and evolving operational requirements. This alignment between project outcomes and organisational priorities increases the overall value and strategic relevance of the initiative.

5.2 Lifecycle Model and Methodology

Given the organisational constraints, stakeholder involvement, and technical nature of the project, a hybrid project management methodology that combines predictive (Waterfall) and adaptive practices has been selected as the most appropriate project management approach for the GreenFields Organics supply chain modernisation initiative.

A predictive approach will be applied to high-level project activities such as project initiation, requirements approval, budgeting, procurement management, scheduling, governance, and milestone control. These activities require formal planning, documentation, approvals, and monitoring to ensure

the project remains aligned with the approved six-month timeline and AUD \$350,000 budget. Structured governance processes, including risk management, quality assurance reviews, vendor management, and formal sign-offs, will also follow a predictive approach to maintain accountability and project control.

At the same time, adaptive and iterative practices will be incorporated during system development, testing and user feedback. Certain project components, particularly such as reporting dashboards, workflow configuration, usability improvement, and user acceptance test may require refinement based on stakeholder input. An iterative approach allows project team to improve system function while ensuring the solution align with operational requirements and expectations.

The project lifecycle will generally follow the phases below:

1. Project Initiation
2. Requirements Gathering and Business Analysis
3. System Design and Planning
4. Development and Configuration
5. Testing and Validation
6. Deployment and User Training
7. Project Closure and Post-Implementation Review

This lifecycle structure aligns with the project's Work Breakdown Structure (WBS), governance framework, quality management, and deployment activities. Iterative feedback loops during testing and validation phases further support continuous improvement while maintaining overall project stability and control.

The hybrid methodology is particularly suitable for this project. This methodology can be used to balance structured governance with adaptive delivery practices and also can be applied to project which require formal planning and flexibility (Project Management Institute, 2021). By combining predictive governance with adaptive delivery practices, the project can maintain strong control while remaining responsive to stakeholder needs and operational realities.

6. REPORT - Scope and Requirements

The scope and requirement plan defines the project boundaries: what work falls within the scope, what is explicitly excluded; Precise scope definition is particularly important given the project's budget and timeline constraints.

a. Project Scope Statement

The GreenFields Organics Supply Chain Modernisation Project covers the planning, design, building, test and delivery of a cloud-based supply chain management system, developed by TechNova Solutions on behalf of the client. The new system will replace GreenFields' reliance on spreadsheets and manual processes with a single integrated digital platform that manages inventory, procurement and logistics across all operational sites. The platform will provide real-time dashboards, automated reorder alerts, purchase order management, supplier tracking and standard management reports accessible to all relevant user roles.

This modernisation project will support multiple user types across the platform; Warehouse staff, senior management will be provided with role-based access control and intuitive user interface. End user training and knowledge transfer sessions will facilitate excellent project handover to ensure consistent adoption across organisation. Given that sensitive operational and supplier data will be hosted in a cloud environment, the platform will follow ISO/IEC 27001 information security principles. ((ISO), 2022)

b. In-Scope Items

The following deliverables and activities are defined within the scope of this project:

- Requirements gathering and business analysis across all operational areas (inventory, procurement, logistics)
- System design including architecture documentation, data models, and user interface wireframes
- Development of a cloud-hosted supply chain management application
- Inventory management module: Stock levels, location tracking, real-time updates
- Procurement module: Purchasing of orders, supplier tracking, approval of workflows
- Logistics module: Delivery scheduling, dispatch tracking, basic reporting
- Automated reorder alerts and low stock threshold notifications
- Stock level dashboards accessible to relevant user roles with real time
- Role-based access control with defined permission levels for all user groups
- Standard management reporting (inventory status, procurement spend, logistics summary)
- System integration testing, user acceptance testing (UAT), and defect resolution

- Deployment to the cloud environment and go-live support
- Legacy data transfer into the new system
- End-user training sessions tailored to each user role
- User manuals, training materials, and technical documentation

c. Out-of-Scope Items

- Hardware procurement or upgrade at any GreenFields site
- Mobile Application development for any platform
- Integration with third-party logistics providers beyond basic data reporting
- Custom report development beyond the agreed standard reporting suite
- Post-deployment hyper-care support

Work Breakdown Structure (WBS)

The Work Breakdown Structure (WBS) diagram below provides a hierarchical decomposition of all project deliverables across five phases: Project Management, Requirements and Design, Development, Testing and Deployment. Here, each level is broken down into two actionable subgroups which are then distributed in smaller chunks of individual deliverables at lowest level. The WBS proves to be the foundational reference document for this project informing project schedule, resource allocation and budget planning. This structure ensures proper alignment between planning and delivery throughout the project lifecycle. The five key phases reflect the full project lifecycle from initial planning, development through to project closure. This system ensures no deliverable is overlooked, responsibilities are clearly assigned and progress can be tracked at a high level and individual level throughout the six-month commitment.

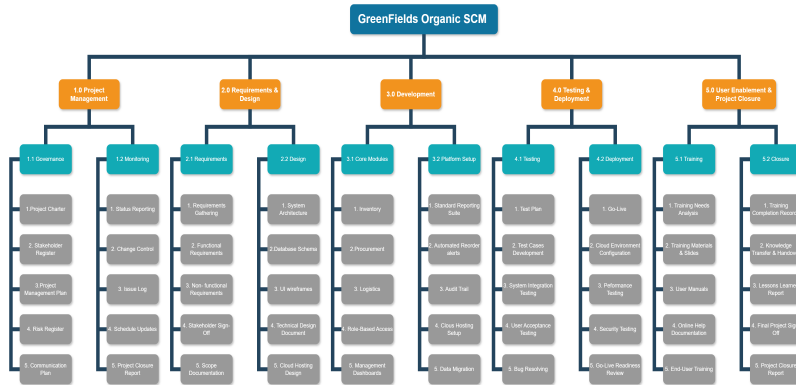


Figure 6.1 - Work Breakdown Structure (WBS)

Table 6.2 - Deliverables Table

WBS Code	Deliverable	Description	Responsible
1.0	Project Management	Overall project coordination, governance and reporting throughout the six-month engagement	Project Manager
1.1	Governance	Project charter, stakeholder register and communication plan	Project Manager
1.2	Monitoring	Status reporting, change control, issue log and schedule updates	Project Manager
2.0	Requirements and Design	Business analysis, system architecture and technical documentation	Business Analyst, Lead Developer
2.1	Requirements Gathering	Stakeholder workshops, requirements documentation, stakeholder sign-off	Business Analyst
2.2	Design	System architecture, database schema, UI wireframes, technical design document, cloud hosting	Lead Developer

3.0	Development	Coding configuration, integration of all system modules and components	Development Team
3.1	Core Modules	Inventory management, procurement and logistics module; Role-based access control, management dashboards	Development Team
3.2	Platform Setup	Standard reporting suite, automated reorder alerts, audit trail configuration, cloud hosting setup, migration of legacy data from spreadsheets	Development
4.0	Testing and Deployment	All testing activities, defect resolution and production deployment	QA Team
4.1	Testing	Test plan, test cases development, system integration testing, user acceptance testing, bug resolving	QA Team
4.2	Deployment	Go-live deployment, cloud environment configuration, performance testing, security testing, go-live readiness review	QA Team, Project Manager
5.0	User Enablement and Project Closure	All training, documentation, handover and formal project closure activities	Training Coordinator, Project Manager
5.1	Training	Training materials and slides, user manuals, online help documentation, end-user training	Training Coordinator
5.2	Closure	Training completion records, knowledge transfer and handover, lessons learned report, final project sign-off, project closure report	Training Coordinator, Project Manager

Key Requirements

Requirements have been prioritised to guide development decisions and manage delivery within the approved budget and six-month guideline. This ensures the most critical system capabilities are delivered first, with lower-priority features considered only after critical features have been completed.

Must Have Features (Delivery is non-negotiable):

These are the core capabilities that directly connect to the GreenFields' business problems: manual entry, delayed management reporting and stock management issues. Without these features the system cannot be accepted, deployed or signed off by GreenField stakeholders.

Should Have Features (High value, included if timeline and budget allow):

These features deliver significant business value but are not critical to system acceptance at go-live. These will be prioritised once all Must Have Features have been completed, tested and approved.

Table 6.3 - Functional Requirements Table

ID	Requirements	Priority	Stakeholder
FR - 01	The platform shall enable warehouse personnel to record and view current stock levels across all GreenFields location without delay	Must have	Warehouse Supervisor
FR - 02	Platform shall notify relevant staff when product quantities drop below a pre-set minimum threshold, triggering a restocking action	Must have	Operations Manager
FR - 03	System should allow authorised user to raise, submit and monitor purchase orders from creation through to confirmed delivery	Must Have	Finance Manager
FR - 04	Platform should restrict access to data and system functions based on each user's designated role	Must Have	CEO / Project Manager

FR - 05	Operational dashboard that refreshes automatically at 15 mins of interval	Must Have	CEO / Operations Manager
FR - 06	System should be deployed entirely within a cloud environment, removing any dependency on local servers at GreenFields facilities	Must Have	TechNova PM
FR - 07	Ability to generate scheduled and on-demand reports for stock status, supplier spend and logistics activity	Must have	Finance Manager
FR - 08	System must maintain an immutable log of all data modifications	Must have	Project Manager / Finance Manager
FR - 09	Platform must run natively in standard web browsers, without additional software	Should Have	Warehouse Supervisor
FR - 10	System should maintain full performance when accessed simultaneously across sites	Should Have	Operations Manager

Table 6.4 - Non-Functional Requirements Table

ID	Requirements	Priority	Stakeholder
NFR - 01	The platform shall have a 99% uptime during GreenFields business operating hours	Must have	CEO/Operations Manager
NFR - 02	System should be designed and hosted in alignment with ISO/IEC 27001 Information security management principles	Must have	Project Manager
FR - 03	User Interface should be intuitive and easy to navigate for non-technical staff	Must Have	Warehouse Supervisor/ Project Manager
FR - 04	Page loads and report generation should be completed within three seconds	Should Have	CEO / Project Manager
FR - 05	The system shall be designed to accommodate growth in user numbers and transaction volumes without structural changes to system architecture	Should Have	CEO

7. REPORT - Time and Cost Management

Project Schedule Overview

The GreenFields Organics Supply Chain Modernisation Project is constrained to a six-month delivery timeline from the date of project initiation. The schedule has been structured across sequential phases, each representing a distinct stage of the project lifecycle. This approach puts deliverables at top priority; Ensuring progress is tracked against defined milestones and scheduled risks are identified early.

Table 7.1 -Project Schedule Overview

Phase	Month(s)	Key Milestone	Deliverable
Initiation	Month 1, Weeks 1-2	Project Charter Approved	Signed Charter, Stakeholder Register
Planning	Month 1, Weeks 3-4	All plans approved	PM plan, Risk register, Communication Plan
Design	Month 2, Weeks 5-8	Design documents signed off	System Architecture, DB Design, UI Wireframes
Development - Sprint 1	Month 3, Weeks 9-12	Inventory module complete	Inventory Management Module
Development - Sprint 2	Month 4, Weeks 13-14	Procurement & Logistics module complete	Procurement Module, Logistics Module
Development - Sprint 3	Month 4, Weeks 15-16	Dashboards & Alerts complete	Dashboard, Automated Alerts, Reporting Suite
Testing - SIT	Month 5, Weeks 17-18	System Integration Test (SIT) passed	SIT report, Bug Fix
Testing - UAT	Month 5, Weeks 19-20	UAT sign-off	UAT Sign-off Document
Training & Deployment	Month 6, Week 21-23	All users and staff trained	Training completion Report, System Go-Live
Closure	Month 6, Week 24	Project formally closed	Closure Report, Lessons Learned, Project Handover

Gantt Chart

The Gantt chart represents the GreenFields Organics Supply Chain Modernisation Project delivery schedule across the full six-month engagement from April 2026 to September 2026. The project schedule is organised across five phases each one consisting of individual work items. Task dependencies are represented through linked bars, which ensures all deliverables are completed and approved. Key project milestones are marked as diamond symbols at the end of each phase; Hence providing clear progress checkpoints for the Project Manager and GreenFields stakeholders throughout the project.

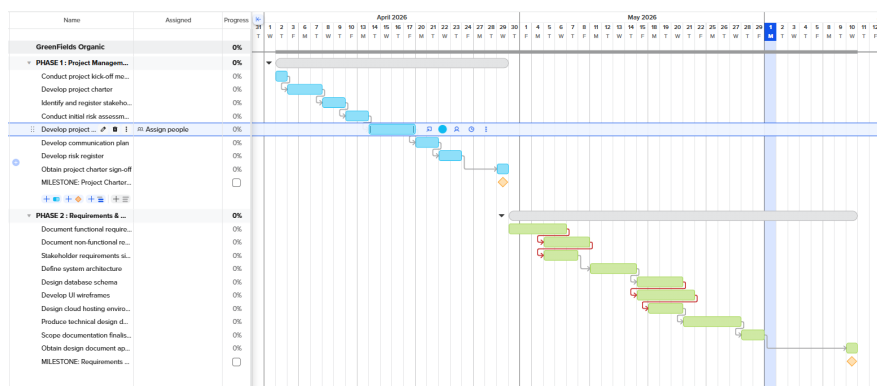


Figure 7.2.1 - Gantt Chart Phase 1 & 2

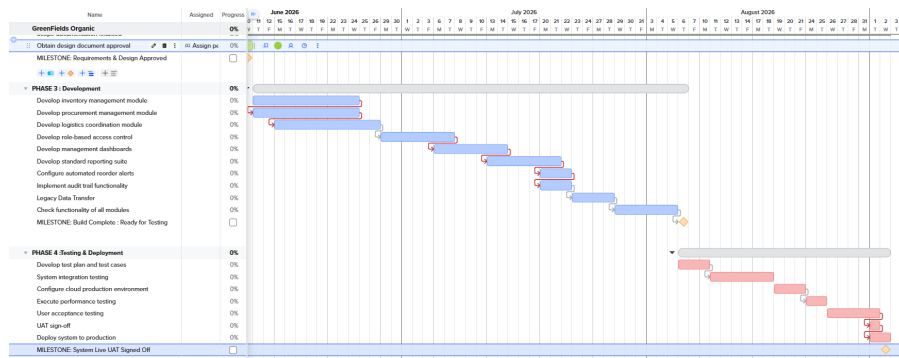


Figure 7.2.2 - Gantt Chart Phase 3 & 4

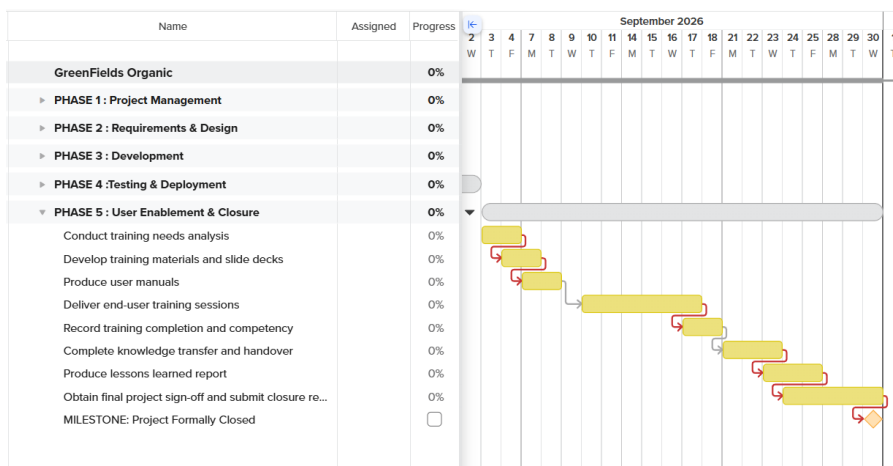


Figure 7.2.3 - Gantt Chart Phase 5

Budget breakdown and allocation

The total approved budget for GreenFields Organics Supply Chain Modernisation project is AUD \$ 350,000; It covers all activities from initiation through to project closure. The budget has been allocated across five cost categories with an additional contingency reserve retained for unforeseen costs or approved scope changes.

Table 7.3.1 - Budget Breakdown Table

Cost Category	Item	Estimated Cost (AUD)	Notes
Labour	Project Manager (@ \$8,500 / month)	\$ 51,000	<u>6 Months</u>
Labour	2 X Business Analyst (@ \$8,000 / month)	\$ 32,000	<u>2 Months</u> for Requirement and Design phase
Labour	3 X Developer (@ \$8,500 / month)	\$ 102,000	<u>4 months</u> for Development through deployment

Labour	2 X QA Tester (@ \$7,500 / month)	\$ 30,000	<u>2 months</u> for Testing phase
Labour	Training Coordinator (@ \$7,000 / month)	\$ 7,000	<u>1 month</u> Training
Software & Licensing	Development Tools, Testing Tools, JIRA licences	\$ 40,000	
Cloud Infrastructure	AWS / Azure	\$ 28,000	Clous-hosted solution
Testing & QA	Performance testing, Security testing, Defect tracking	\$ 21,000	SIT, UAT
Training & Documentation	Training material, User manuals	\$ 21,000	KTs, Recordings
Contingency	Reserved for unforeseen costs	\$18,000	Through formal change process
	TOTAL	\$ 350,000	

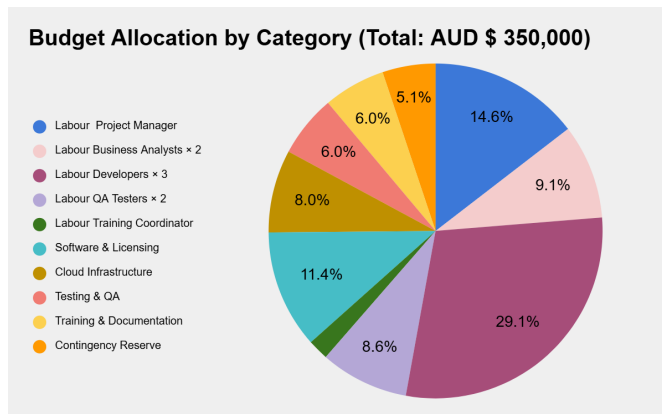


Figure 7.3.2 - Pie Chart: Budget Allocation by category

The pie chart illustrates the proportional allocation of the total approved budget of AUD \$350,00. The Labour - Developers represents the highest 29.1% share, reflecting the intensive development phase of four months. Labour - Project Manager is involved throughout six months and account for 14.6% of budget. Business Analysts and QA Testers represent 9.1% and 8.6% respectively. Software and Licensing accounts for 11.4% which covers development tools, testing tools and JIRA licences. Cloud infrastructure, Testing & QA and Training and Documentation each cost between 6.0% and 8.0% of the total budget. A contingency reserve of \$18,000(5.1%) has been kept aside to address unforeseen costs through formal change control process.

8. REPORT - Risk Management

Effective risk management is important to the success of the GreenFields Organics supply chain modernisation project. Considering the project's constraints which are AUD\$350,000 Budget, 6-month timeline and new IT System across multiple sites, the project's risk environment is both highly diverse and complex. A structured approach to managing risk in accordance with PMBOK was employed on this project including identifying risks, conducting qualitative assessments of those risks, developing plans of action and continuously assessing the risks during the life cycle of the project. A likelihood-impact matrix was used to evaluate each identified risk to establish a total risk rating for that particular risk. Each mitigation strategy developed for this project has focused on reducing either the probability or the impact of each identified risk prior to its occurrence.

Below is a list of all identified risks that have been documented within the risk register. The risk owners are responsible for continually reviewing and addressing their respective risk assignment

Table 8.1 - Risk register

Risk ID	Risk Description	Category	Likelihood	Impact	Risk rating	Existing controls	Mitigation	Contingency	Risk owner
R-01	Scope creep from evolving stakeholder requirements	Schedule/Scope	High	High	Critical	Project charter defines scope	Formal change control process, regular scope reviews, sign off on all change requests	Escalate to project sponsor, rebase line schedule and budget if changes approved	Project manager
R-02	Delays in stakeholder sign-off on requirements causing schedule impact	Schedule	Medium	High	High	Weekly stakeholder check-ins planned	Set clear sign off deadlines, involve stakeholders early in requirements workshops	Compress development phases or negotiate timeline extension	Business analyst
R-03	Limited IT infrastructure at GreenFields sites causing integration/deployment issues	Technical	High	High	Critical	Preliminary site assessment planned	Infrastructure assessment during initiation, cloud based deployment to minimise on premise dependency	Provision temporary infrastructure or engage external vendors	Lead Developer
R-04	Budget overrun from underestimated effort or unanticipated vendor costs	Budget	Medium	High	High	Initial cost estimation completed	10-15% contingency reserve, regular budget tracking, fixed price vendor	Descope lower priority features, seek additional funding	Project manager

Commented [SH9]: Change the pages that the risk register is on to landscape please

							contracts where possible		
R-05	Low user adoption due to resistance from warehouse/operational staff	Stakeholder	High	Medium	High	Training coordinator assigned	Involve end users in UAT, tailored training materials by proficiency level	Additional post deployment support	Training coordinator
R-06	Data migration errors or loss of historical inventory/procurement data	Technical	Medium	Critical	Critical	Data migration plan to be developed	Detailed migration plan with pre and post validation, parallel running of old and new systems during transition	Restore from verified backups	Lead developer
R-07	Security vulnerabilities or data privacy breaches in the supply chain system	Compliance/Security	Low	Critical	High	Data privacy requirements documented	Security by design, penetration testing before go live, compliance with Australian Privacy Act 1988	Invoke incident response plan, notify affected parties, engage cybersecurity specialist	PM/Lead developer

R-08	Key team member departure during critical project phases	Resource	Low	High	Medium	Task Allocation Agreement in place	Document knowledge throughout project, cross train team members on critical tasks	Engage replacement contractor, redistribute tasks among remaining team	Project manager
R-09	Vendor delays in delivering software licences or cloud hosting	Procurement	Medium	Medium	Medium	Vendor shortlist to be prepared	Contracts with clear SLAs and delivery milestones, engage backup vendors during selection	Source alternative vendor, negotiate accelerated delivery	Procurement lead
R-10	Inadequate testing leading to post-deployment defects	Quality	Medium	High	High	QA/Testing team assigned	Comprehensive test plan, defined entry and exit criteria per phase	2-4 week dedicated post deployment support period	QA/Test lead

9. REPORT - Quality Management

The GreenFields Organics supply chain modernisation project's quality management encompasses ensuring that all project deliverables meet the specified functional capabilities and the agreed-upon performance criteria.

It further ensures that all stakeholder needs and expectations are met. This section addresses the quality objectives, quality assurance processes, quality control activities and key metrics which will be used as the basis for project quality management.

In addition to the alignment with the knowledge areas of the PMBOK, all quality management activities will also follow a PDCA (Plan-Do-Check-Act) cycle throughout the project life cycle.

The overall quality goal of the project is to develop a complete, reliable and user-friendly supply chain management system in accordance with the agreed scope, schedule and cost, and that meets all applicable data privacy laws and regulations.

Quality Objectives

- All functional requirements identified in the approved requirements specification are implemented and validated by means of formal testing prior to launching the system.
- The System shall achieve a defect resolution rate of at least 95% for critical and high severity defects prior to deployment.
- Formal review and approval of training materials and user manuals will be done by both the training coordinator and at least one representative end-user from each of the user groups.
- The system will comply with all applicable data privacy laws, specifically the Australian Privacy Act of 1988.

Quality Assurance

Quality Assurance (QA) is responsible for ensuring that the methodologies used to create an application are correctly followed. This is accomplished through several reviews:

- Requirements reviews: A thorough walk-through of all requirements documentation with all appropriate stake holders will take place before any development begins to ensure all requirements have been clearly defined and understood.
- Design reviews: All technical design documents will also include a review from at least another developer, before they begin implementing their design.
- Code reviews: Once a module of code has been completed and prior to entering into the test phase, it will undergo a peer-review by another developer to identify errors as soon as possible in the software life cycle.

- Test plan review: A formal review and approval of the test plan will occur by both the project manager and the QA Lead before any testing is conducted.
- Post implementation review: Upon completing the project, a formal quality review will take place to determine whether quality objectives have been met and where improvements can be made on future projects.

Quality Control

Quality control (QC) involves the inspection and testing of all the project deliverables is completed to ensure that they meet the established quality standards.

- Unit testing: Developers will test individual components once they are complete.
- Integration testing: All interfaces between system modules, inventory, procurement and logistics will be tested to ensure that all modules work together properly.
- User acceptance testing (UAT): End-users from each stakeholder groups will perform user acceptance testing to determine if the system is meeting their operational requirements. UAT will take place over a two week time frame prior to deploying the system.
- Regression testing: Any changes or fixes to defects that occur during the testing phase will be subjected to regression testing to ensure that no additional defects have occurred.
- Performance testing: The system will be tested at loads consistent with what has been estimated to confirm response time and overall system stability meet established criteria.

Table 9.1 - Quality metrics

Metric	Description	Target	Measurement method	Frequency	Responsible
Requirements traceability	% of approved requirements covered by test cases	100%	Requirements Traceability Matrix	At start of testing phase	QA/Test Lead
Defect resolution rate (Critical/High)	% of critical and high defects resolved before go-live	> 95%	Defect tracking log	Weekly during testing	QA/Test Lead

UAT sign-off	Formal sign-off received from all key stakeholder representatives	100%	UAT sign-off form	End of UAT phase	Project manager
Test coverage	% of functional modules covered by test cases	> 90%	Test Plan review	At start of testing phase	QA/Test Lead
Training material approval	Training materials reviewed and approved by end user representatives	100%	Review sign-off record	Prior to training delivery	Training coordinator
Post deployment defects	Number of critical defects identified within 4 weeks of go-live	0 critical defects	Helpdesk incident log	Weekly post deployment	QA/Test Lead
Data migration accuracy	% of records successfully migrated and validated	> 99.5%	Data validation report	Post migration	Lead developer

10. REPORT - Procurement Management

In order to support the TechNova Solutions project team in providing all the required products and services to complete the GreenFields Organics supply chain modernisation project, multiple external products and services need to be acquired. All procurements for this project will be carried out within the constraints of the projects time-line and budget as well as regulatory and legislative requirements. In addition, all purchases made during the project will be formally recorded, evaluated based on predetermined evaluation criteria and approved by the project manager and Greenfields project sponsor prior to contract award.

Products & services to be procured

The decision was made to use a cloud deployment model for this project due to its ability to scale, reduce reliance on on-site infrastructure and align with the limited capacity available at GreenFields for on-site IT functions. Based upon these factors, the following procurement items were determined to be necessary.

Table 10.1 - Procurement items

Item	Type	Justification
Cloud hosting services	Service	Required to host the supply chain management system
Supply chain management software licence or SaaS subscription	Software or license	Core software platform to be configured and deployed for GreenFields, reduces custom development effort and risk
Data migration tools / services	Service / software	Specialised tooling or contracted services required to safely migrate existing inventory and procurement data from spreadsheets to the new system
Cybersecurity / penetration testing service	Service	Independent security testing to be conducted prior to go-live to ensure compliance with the Australian Privacy Act 1988 and data security requirements
Post deployment support contract	Service	Vendor or third-party support services to provide technical assistance during the post-deployment stabilisation period

Vendor selection criteria

Prior to engaging with a vendor, all vendors will be evaluated using the following weighted evaluation criteria. Formal Requests for Quotes (RFQ) or Requests for Proposals (RFP) will be used for larger value acquisitions.

Table 10.2 - Vendor selection criteria

Criterion	Weighting
Technical capability and fit	30%
Cost and value for money	25%
Vendor reputation and experience	20%
Security and compliance	15%
Support and SLA commitments	10%

Vendor management strategy

Once vendors have been involved, the following will be used to control vendor relationships during the life cycle of this project:

- Contracts with service level agreement (SLA): Each contract that is made with a vendor will contain an SLA which includes specific details about what needs to be delivered as well as what type of service level can be expected at all times.
- Monthly progress meetings: On a monthly basis, the Project Manager will schedule meetings with those vendors who play a significant role in meeting the objectives of this project, specifically the vendors responsible for cloud-hosting services and providing software applications.
- Single point of contact: For purposes of efficient communication and resolving issues associated with a particular vendor, one person will serve as the single point of contact for both TechNova and each vendor organisation.
- Vendor performance monitoring: During this project, vendor related risk factors will be closely monitored. In the event that a vendor does not meet its obligation regarding timely delivery, the contingency plan for sourcing alternative vendors will be initiated.
- Invoice and budget Tracking: Before issuing payment on any invoice received from a vendor, it shall be reviewed for compliance with contracted pricing and approval shall be obtained from the project manager.

11. REPORT - Execution, Governance, and Monitoring

This section outlines the execution, governance and monitoring processes that will be employed to achieve the GreenFields Organics Supply Chain modernisation project objectives in a timely manner, within budget and to meet the agreed upon quality standards.

11.1 Governance and Roles

The project governance structure defines the decision making levels, accountability lines and procedures of escalation for the project. TechNova Solutions is operating as the delivering organisation for this project, while GreenFields Organics is represented by its senior client stakeholders who have formal approval authority for significant project decisions.

Levels of Governance:

- **Project sponsor** (GreenFields CEO) - ultimately accountable for all aspects of project success and escalation point for unresolved Issues. Approves the project charter, major changes to scope and budget variations.
- **Project manager** (TechNova) - responsible for day to day oversight of the project. Also responsible for schedule management, budget management, risk management and stakeholder management. Chairs weekly project status meetings.
- **Project team** (TechNova) - Each member has responsibility to execute their respective deliverables as outlined in the project plan.
- **Client representatives** (Green Fields) - Operations manager, finance manager and warehouse supervisor participate in requirements workshops, user acceptance testing and sign off on project deliverables.

Table 11.1 - RACI Chart

Activity	Project mgr	Business analyst	Developer	QA/Test lead	Training Coordinator	GreenFields CEO	Operations manager	Finance mgr	Warehouse supervisor
Project charter approval	A	C	-	-	-	R	C	C	-
Requirements gathering	R	A	C	-	C	-	C	C	C
System design	A	R	-	-	-	-	I	I	-
Development	I	C	R/A	C	-	-	-	-	-
Testing (QA)	A	C	C	R	-	-	I	I	-
User acceptance testing	A	C	C	R	C	-	R	R	R
Training delivery	A	-	-	-	R	-	I	I	I
Go live approval	A			C		R	C	C	
Post deployment review	R/A	C	C	C	C	I	C	C	C
Change request approval	A	C	C	C	-	R	C	C	-

R = Responsible, A = Accountable, C = Consulted, I = Informed

11.2 Communication Plan

Communication plays an important role in maintaining alignment with all stakeholders involved through out the life cycle of this project. The project level communications plan below (in Table 11.2) will outline the type of communication channels, frequency, audience, and purpose for all key communications during the project.

Table 11.2 - Project communication plan

Communication type	Purpose	Audience	Channel	Frequency
Project status meeting	Review progress, issues and upcoming activities	TechNova project team	Microsoft Teams	Weekly
Stakeholder status report	Update client on progress, risks, milestones	GreenFields CEO, operations manager, finance Manager	Email	Fortnightly
Requirements workshop	Gather and validate business requirements	Business analysts, GreenFields stakeholders	In person / Teams	As required
Risk review	Review and update risk register	Project manager, relevant risk owners	In person	Fortnightly
UAT feedback sessions	Gather user feedback during acceptance testing	QA lead, end users	In-person / Teams	During UAT phase
Change request	Inform approved or rejected changes	Project sponsor, stakeholders	Email + change Log	As required
Project closure report	Formally close project and document outcomes	GreenFields CEO, TechNova management	Formal written report	End of project

11.3 Progress Tracking and Change Control

Progress tracking

Project performance will be monitored on a continuous basis using earned value management principles and the key performance indicators (KPIs) defined below.

Table 11.3.1 - KPIs and performance metrics

KPI	Description	Target	Measurement method	Frequency
Schedule Performance Index (SPI)	Measures schedule efficiency (earned value / planned Value)	≥ 0.9	Project scheduling tool	Fortnightly
Cost Performance Index (CPI)	Measures budget efficiency (earned Value / actual cost)	≥ 0.9	Budget tracking spreadsheet	Fortnightly
Milestone completion rate	% of planned milestones completed on or before due date	100% on time	Gantt chart review	Monthly
Open issues / defects	Number of unresolved issues or defects logged	0 critical unresolved at milestone gates	Issue and defect log	Weekly (testing phase)
Change requests processed	Number of requests submitted, approved and implemented	Processed within 5 days	Change log	As required
Stakeholder satisfaction	Feedback from GreenFields stakeholders on project progress	Positive feedback at milestone review	Verbal or written feedback at milestone reviews	At each milestone

Change Control

All project scope, time schedule, financial budget and major project deliverable adjustments should be made through the formally defined change control procedure. No changes will be made without approval of documented change requests by project team members or stakeholders.




Figure 11.3.2 - Change Control Process

Table 11.4

Field	Details
Change Request ID	CR-001
Date submitted	DD/MM/YYYY
Submitted by	[Name / role]
Description of change	[Brief description of the proposed change]
Reason / justification	[Why is this change needed?]
Impact on scope	[Describe any change to project deliverables or boundaries]
Impact on schedule	[Estimated change to timeline, e.g., +5 days]
Impact on budget	[Estimated cost impact, e.g., +AUD \$5,000]
Impact on risk	[Any new or changed risks introduced by this change]
Recommended action	Approve / reject / defer
Approved by	[Project manager / project sponsor]
Approval date	DD/MM/YYYY
Status	Submitted / under review / approved / rejected / implemented

11.4 Tools and Software

The following tools and software will be used to support project execution, scheduling, collaboration and documentation throughout the project lifecycle.

Table 11.5 - Project tools and software

Tool / software	Purpose
Microsoft Project / GanttPRO	Project scheduling, gantt chart creation, milestone tracking and progress monitoring
Microsoft Teams	Team communication, virtual meetings, file sharing and collaboration across TechNova and GreenFields stakeholders
Microsoft SharePoint / OneDrive	Centralised document management and version control for all project documentation
Jira (or equivalent)	Issue tracking, defect logging and sprint management during development and testing phases
Microsoft Excel	Budget tracking, risk register maintenance and data migration validation
Confluence (or equivalent)	Knowledge base and documentation repository for technical design documents, meeting minutes and project artefacts
Zoom / Teams Video	Stakeholder meetings and UAT sessions with GreenFields representatives at remote sites

12. REPORT - Project Closure and Knowledge Transfer

12.1 Closure Activities

The closure phase of the project ensures that all the required deliverables are fully completed, validated and handed over to the organization successfully.

The closure activities that will be conducted are:

1. **Final Deliverable Acceptance:** The complete supply chain management system will be review against the defined requirements and the scope. Then, formal acceptance will be obtained from the stakeholders, including CEO, Operations Managers and Finance Manager.
2. **System Validation and Signing off:** Confirmation will be obtained about all the criteria being met, including completion of User Acceptance Testing and system performance benchmarks.
3. **Administrative Closure:** All the project documentation will be finalized and archived for any future organizational reference.
4. **Final Closure:** A final review of the project budget will be conducted so that all the costs are accounted for and approved. Any differences will be analysed.

5. **Release of Resources:** All the project members from NovaTech Solutions and the internal staff will be formally released and transitioned back to their respective roles.
6. **Post Implementation Review:** A review will be conducted to evaluate the project performance against key criteria.

12.2 Lessons Learned

Table 12.2 - Lessons Learned

Category	Lesson Learned
Project Planning	Importance of defining detailed scope upfront to prevent any potential scope creeps.
Stakeholder Engagement	Engagement with end users frequently and early is critical for user adoption.
Technology	Selection of cloud platform vendor should begin very early; in Week 1. The procurement lead times are longer than estimated.
Risk Management	Data migration risks were underestimated initially, therefore, a dedicated data quality assessment in planning would reduce such risks.
Team Collaboration	Instead of having a single team lead and review, rotating these roles improve team collaboration and documentation.
Change Control	Formal change control prevented scope creep in Month 3, when additional analytics module was requested by GreenFields, helping the budget and timeline be on track.

12.3 Knowledge Transfer Plan

Table 12.3 - Lessons Learned

Knowledge Asset	Transfer Method	Recipient	Responsible
System User Manuals (All roles)	PDF and online help within the system	All the users	Shreyas Dhakal
System Administrator Guide	Detailed technical documentation provided to GreenFields IT team	GreenFields IT Representatives	Sheikh Muhammad Aarib

Source Code and Documentation	Deposited in the repository; credentials handed over	GreenFields IT Representatives	Sheikh Muhammad Aarib
Vendor Contacts and SLA	List of vendor contacts, documents of SLA provided	GreenFields Operation Manager	Hari Prasad KV
Training Delivery Materials	Training slides, documents and recordings provided to GreenFields.	GreenFields Training Representative	Xinxin Dong
Project Documentation Archive	Complete project document archive via shared OneDrive folder.	GreenFields Operations Manager	Avishkar Waikar

13. REPORT - Ethical, Cultural, and Professional Considerations

13.1 Ethics and Professional Responsibility

The project team is committed to maintaining the highest ethical and professional standards throughout delivery. All the team members of TechNova are expected to adhere to the Australian Computer Society (ACS) Code of Ethics, which establishes principles of honesty, competence, professional development, public interest, and respect for stakeholders. (ACS, 2023)

A key ethical obligation is the responsible handling of sensitive operational data of GreenFields available commercially. The project team will implement data governance protocols, including encrypted data storage and transmission, and handling procedures compliant with the Privacy Act 1988 (Australia, 1988) and the Australian Privacy Principles (APPs). A Privacy Impact Assessment (PIA) will be performed during design to identify and mitigate privacy risks before the system is built. (Commissioner, 2020) (Majka)The project team will be transparent to the client at all times, with constant reporting and disclosing any issues, delays or risks. The vendor agreements will be conducted through a fair and competitive procurement process.

13.2 Cultural and Diversity Considerations

The project team comprises members with diverse cultural and professional backgrounds, which is a major strength of the team. With more diverse team, a team provides more innovative solutions, and serve diverse client needs). The team has established inclusive communication norms; including

rotating meeting chairs, equal speaking opportunities, and respectful disagreement protocols — to ensure all members' contributions are prioritised equally.

GreenFields Organics employs staff with different levels of technical literacy, ranging from senior management team to warehouse and logistic personnel. The team will adopt culturally inclusive approach for user engagement, training and ensure that the materials are in a plain, jargon-free and accessible language.

Change management is equally a major cultural challenge as a technical one. So, the user resistance to new systems is well-documented, particularly where manual processes have been used for a long time. The team will involve end users actively throughout design, testing and training to build ownership and also reduce resistance, drawing on the Prosci ADKAR Model. (Majka)

13.3 Sustainability & Social Impact

The digital transformation of GreenFields' supply chain has highly significant benefits. Replacing the paper-based processes by a digital system, the project reduces paper consumption and its associated environmental footprint. Improving inventory management will reduce waste resulting from overstock and stockouts situation, which is a direct contribution to GreenFields' objectives of sustainability and the United Nations Sustainable Development Goal 12: Responsible Consumption and Production. Improving supply chain visibility will also support GreenFields in making more informed procurement decisions, including the ability to track performance of supplier and sustainability credentials over time. The team is committed to minimising its own environmental footprint by conducting meetings virtually as much as possible.

14. REPORT - Conclusion and Recommendations

14.1 Conclusion

The GreenFields Organic Supply Chain Modernisation Project represents an important digital transformation initiative for agricultural business for regional areas seeking to expand beyond manual, spreadsheet-based process. The Project Management Plan presented in this report demonstrates a detailed and comprehensive, PMBOK aligned approach to planning and delivering this initiative within the time and cost constraints of six months and AUD \$350,000.

The plan covers all key knowledge areas: scope management, time management, cost management, risk management, quality management and procurement management, using various tools and

techniques like WBS, requirements register, Gantt chart, etc. For this project's context, selection of a hybrid project lifecycle model, with a combination of predictive planning governance with Agile iterative development is appropriate, as it balances the need for client approval of requirements and design documents with the flexibility to incorporate user feedback during development. The engagement and communication strategies ensures that all parties; from GreenFields CEO to warehouse staff, receive proper timely information throughout. The team is confident that, when executed with accordance with this plan, the project will deliver measurable value to GreenFields Organics and serve as a strong reference case for TechNova Solutions in the agricultural business sector.

14.2 Recommendations

1. Assign a dedicated Change Champion for GreenFields, ideally the Operations Manager, so that they can lead internal communications about the new system. Using internal champions are an indicator of critical success factor for enterprise system adoption.
2. Vendor selection and SaaS platform procurement should be commenced in Week1 of the project. Extending this period risks compressing the development timeline.
3. Before commencing data migration, a formal Data Quality Assessment should be conducted for the existing spreadsheet. Any unresolved data quality issues are the leading cause of defects in SCM implementations.
4. A 4-week post-go-live period should be established for hypercare, during which TechNova staff should be readily available to assist the GreenFields users. This should be budgeted within the management reserve.
5. Following project closure, GreenFields should encourage a provider to develop a IT governance framework and agreement of system maintenance to ensure the long-term viability of the delivered solution.
6. A user satisfaction survey should be conducted at a month mark after live deployment to assess adoption rates and identify any remaining training needs, using results to determine whether additional investment or effort is required.

Commented [SH10]: Overall, some good work present. Please make sure font, format and presentations are consistent throughout the document.

15. MINUTES OF MEETINGS

15.1 Meeting 1

Date: 02/04/26

Time: 4:12pm - 5:00pm

Location: UB35, Nexus10, Adelaide City Campus East

Chair/Coordinator: Sheikh Muhammad Aarib Azfar

Attendees

Hariprasad K V, Xinxin Dong, Shreyas Dhakal, Avishkar Waikar

Apologies

None

Agenda

- Go through the available report and resources
 - Read the full report
- Setup shared OneDrive folder
 - Setup of OneDrive folder completed, and the access was given to all the team members, along with required communication plan.

Post Meeting Action Items

Action	Assigned To	Deadline
Go through resources and report	Everyone	09/04/26
Setup shared OneDrive folder	Aarib	09/04/26

Decisions Made

- Team roles allocated as documented.
- Cloud-based SaaS approach identified as the preferred technical direction.

Next Meeting

Next Meeting: 09/04/26 on 3:00pm at UB35, Nexus10, Adelaide City Campus East

15.2 Meeting 2

Date: 09/04/26

Time: 4:12pm - 5:00pm

Location: UB35, Nexus10, Adelaide City Campus East

Chair/Coordinator: Shreyas Dhakal

Attendees

Hariprasad K V, Xinxin Dong, Avishkar Waikar, Sheikh Muhammad Aarib Azfar

Apologies

None

Agenda

- Review assignment requirements
 - The team reviewed the GreenFields Organics Case Study
- Finalise the project topic and direction of the project
 - There was an agreement to focus on the supply chain modernisation project.
- Assigning of initial sections and responsibilities.
 - Discussion of structure of the report and deliverables.

Post Meeting Action Items

Action	Assigned To	Deadline
Finalise project background and response	Xinxin	13/04/2026
Draft Objectives and Success Criteria	Avishkar	13/04/2026
Start Team Documents	Aarib	13/04/2026
Assist with documentation	Hari	13/04/2026

Commented [SH11]: information here is missing.

Commented [MS11R2]: It seems your team have not completed the meeting notes or there has been no work done. There has no action plan required for the next meeting.

Decisions Made

- Project topic confirmed
- Work will be divided based on strengths

Next Meeting

Next Meeting: 16/04/2026

15.3 Meeting 3

Date: 16/04/2026 4:12pm - 5:00pm UB35, Nexus10, Adelaide City Campus East

Time: 4:12pm - 5:00pm

Location: UB35, Nexus10, Adelaide City Campus East

Chair/Coordinator: Avishkar Waikar

Attendees

Hariprasad K V, Xinxin Dong, Shreyas Dhakal, Sheikh Muhammad Aarib Azfar

Apologies

None

Agenda

- Review progress on Project overview section
 - Background, objectives and justification are drafted
- Starting of Scope and Requirements section
 - Identification of key system features
- Discussion of WBS and deliverables
 - Discussion of in-scope and out-of-scope items

Post Meeting Action Items

Action	Assigned To	Deadline
Complete scope and requirements	Avishkar, Aarib	20/04/26
Draft Project Charter	Xinxin	20/04/26
Review and Edit Section	Shreyas	20/04/26
Support scope drafting	Hari	20/04/26

Decisions Made

- Finalization of scope inclusions
- Exclusion of hardware/mobile development

Next Meeting

Next Meeting: 23/04/2026

15.4 Meeting 4

Date: 23/04/2026

Time: 7:00 pm to 8:30 pm

Location: Google Meet

Attendees

Hariprasad K V, Xinxin Dong, Shreyas Dhakal, Sheikh Muhammad Aarib Azfar

Apologies

None

Agenda

- Progress on Strategy, Time and Cost
 - Discussion of lifecycle model; hybrid approach
- Begin Risk and Quality Management
 - Identification of Potential Risks and Mitigation Approaches

Post Meeting Action Items

Action	Assigned To	Deadline
Drafting of time and cost section	Avishkar, Hari	27/04/26
Prepare risk register	Hari, Aarib	27/04/26
Drafting of Quality Management	Aarib	27/04/26
Editing and Formatting	Shreyas	Ongoing

Decisions Made

- Use of structured PMBOK framework
- Adopt likelihood-impact matrix of risk analysis

Next Meeting

Next Meeting: 30/04/2026

15.5 Meeting 5

Date: 30/04/2026

Time: 5:00 – 6:00pm

Location: Google Meet

Chair/Coordinator: Aarib

Attendees

Hariprasad K V, Xinxin Dong, Shreyas Dhakal, Sheikh Muhammad Aarib Azfar

Apologies

None

Agenda

- Review Risk, Quality and Procurement sections
 - Confirmation of Risk Register Structure
- Starting of Execution and Governance

Post Meeting Action Items

Action	Assigned To	Deadline
Finalize Risk Management	Hari	03/05/2026
Complete Quality Management	Aarib	03/05/2026
Draft Procurement Section	Hari	03/05/2026
Start Governance Section	Shreyas	03/05/2026

Decisions Made

- Include SLA and vendor monitoring strategies
- Add QA/QC processes

Next Meeting

Next Meeting: 03/05/2026

15.6 Meeting 6

Date: 03/05/2026

Time: 9:00 – 10:00 PM

Location: Google Meet

Attendees

Hariprasad K V, Xinxin Dong, Shreyas Dhakal, Sheikh Muhammad Aarib Azfar

Apologies

None

Agenda

- Review Execution and Monitoring Section
 - Communication plan to align with team communication table.
- Plan Closure and Ethical Sections
 - Discussion of project closure activities and knowledge transfer

Post Meeting Action Items

Action	Assigned To	Deadline
Completion of Execution and Governance	Shreyas	06/05/2026
Draft Closure and Knowledge Transfer	Shreyas	06/05/2026
Draft Cultural and Ethics Sections	Avishkar	06/05/2026

Decisions Made

- Use weekly tracking and change control approach
- Include KPIs so that there is effective monitoring

Next Meeting

Next Meeting: 10/05/2026 8:30-10:00 AM

15.7 Meeting 7

Date: 10/05/2026

Time: 8:30-10:00 AM

Location: Barr Smith Library Level 1A

Chair/Coordinator: Avishkar Waikar

Attendees

Hariprasad K V, Xinxin Dong, Shreyas Dhakal, Sheikh Muhammad Aarib Azfar

Apologies

None

Agenda

- Project Closure Planning
 - Shreyas led closure, ethics and conclusion section
- Lessons learned
 - Discussion of lessons learned and knowledge transfer

Post Meeting Action Items

Action	Assigned To	Deadline
Complete Closure Section	Shreyas	13/05/2026
Draft Ethics Section	Shreyas	13/05/2026
Review Content	Avishkar, Aarib	13/05/2026

Decisions Made

- Include structured lessons learned
- Focusing on compliance and data protection

Next Meeting

Next Meeting: 16/05/2026

15.8 Meeting 8

Date: 16/05/2026

Time: 9:00 – 10:00 PM

Location: Google Meet

Chair/Coordinator: Shreyas Dhakal

Attendees

Hariprasad K V, Xinxin Dong, Shreyas Dhakal, Sheikh Muhammad Aarib Azfar

Apologies

None

Agenda

- Final Editing
 - Avishkar performed the final editing of report and presentation
- Verify all Sections
 - All members reviewed the work

Post Meeting Action Items

Action	Assigned To	Deadline
Final Proofreading	All members	25/05/2026
Final Editing	Avishkar	25/05/2026

Decisions Made

- Approval of final document by all the members

Word count: 11,770

REFERENCES

- (ISO), I. O. (2022). *International Organization for Standardization (ISO) Title: Information security, cybersecurity and privacy protection — Information security management systems — Requirements (ISO/IEC 27001:2022)*. ISO/IEC.
- ACS. (2023). *ACS Code of Professional Ethics*.
- Australia, C. o. (1988). *Privacy Act 1988*. Canberra: Commonwealth of Australia.
- Commissioner, O. o. (2020). *Guide to undertaking privacy impact assessments*. Retrieved from Office of the Australian Information Commissioner: <https://www.oaic.gov.au>
- Kerzner, H. (2022). *Project Management: A Systems Approach to Planning, Scheduling, and Controlling*. Hoboken, New Jersey, USA: Wiley.
- Majka, M. (n.d.). *Facilitating Successful Change: A Comprehensive Guide to the ADKAR*. 2024.
- Mints, A., & E. K. (2019). Methods of stakeholder prioritisation in the context of stakeholder management.
- Project Management Institute. (2021). *A Guide to the Project Management Body of Knowledge*. Newtown Square, Pennsylvania, USA: Project Management Institute.
